


# CDR Maguire

## Franklin Regional Transit Authority -Critical Milestones


WBS	ID	Task Name	Start	Finish	Duration	Predecessors	Total Slack	1st Quarter		3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter	
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
DEP	1	<b>Design Procurement</b>	Fri 6/2/17	Fri 10/6/17	90d		10.5d																									
DEP.010	2	A/E Procurement	Fri 6/2/17	Fri 10/6/17	90d		1139d																									
DEP.020	3	Public Advertisement/Newspaper	Fri 6/2/17	Fri 6/30/17	20d		1383.5d																									
DEP.050	4	Conduct A/E Site Bid Conference	Mon 6/19/17	Mon 6/19/17	1d		0d																									
DEP.030	5	Proposal Due	Tue 8/1/17	Tue 8/1/17	0d	4FS+31d	0d																									
DEP.040	6	Review Committee - Shortlisted A/E's	Wed 8/2/17	Tue 8/15/17	10d	5	0d																									
DEP.070	7	Interview A/E - Selection	Fri 8/18/17	Fri 8/18/17	0d	6FS+3d	0d																									
DEP.080	8	A/E Contract Award	Mon 8/28/17	Mon 8/28/17	0d	7FS+6d	0d																									
DE	9	<b>Design Activities</b>	Tue 8/29/17	Mon 7/16/18	229d		0d																									
DE.010	10	NTP to A/E	Tue 8/29/17	Tue 8/29/17	0d	8FS+1d	0d																									
DE.020	11	Programing and Site Analysis	Wed 8/30/17	Tue 9/12/17	10d	10	0d																									
DE.030	12	Schematic Design	Wed 9/13/17	Mon 10/16/17	24d	11	0d																									
DE.040	13	Schematic Design Submission	Mon 10/16/17	Mon 10/16/17	0d	12	0d																									
DE.050	14	Design Development	Tue 10/17/17	Mon 1/8/18	60d	13	0d																									
DE.051	15	CDR Maguire Cost Estimate	Tue 10/17/17	Mon 1/8/18	60d	14SS	30d																									
DE.052	16	Construction Documents	Tue 10/17/17	Mon 2/19/18	90d	14SS	0d																									
DE.053	17	Design Development Submittal	Mon 2/19/18	Mon 2/19/18	0d	16,14,15	0d																									
DE.054	18	Design Development Review by CDRM	Tue 2/20/18	Mon 3/12/18	15d	17	0d																									
DE.060	19	Develop 60% Construction Documents	Tue 3/13/18	Mon 5/14/18	45d	18	0d																									
DE.061	20	60% Construction Documents Submittal	Mon 5/14/18	Mon 5/14/18	0d	19	0d																									
DE.062	21	60% Construction Documents Review by CDRM	Tue 5/15/18	Mon 6/4/18	15d	20	0d																									
DE.090	22	Develop 90% Construction Documents	Tue 6/5/18	Mon 6/25/18	15d	21	0d																									
DE.091	23	90% Construction Documents Submittal	Mon 6/25/18	Mon 6/25/18	0d	22	0d																									
DE.092	24	90% Construction Documents Review by CDRM	Tue 6/26/18	Mon 7/16/18	15d	23	0d																									
DE.100	25	Design Completion	Mon 7/16/18	Mon 7/16/18	0d	24	0d																									
COP	26	<b>Construction Procurement</b>	Wed 7/18/18	Wed 9/26/18	51d		0d																									
COP.010	27	Bidding	Wed 7/18/18	Mon 9/17/18	44d	25FS+1d	0d																									
COP.020	28	Bids Due	Mon 9/17/18	Mon 9/17/18	0d	27	0d																									
COP.030	29	Award Construction Contract	Wed 9/26/18	Wed 9/26/18	0d	28FS+7d	0d																									
CON	30	<b>Construction</b>	Tue 10/2/18	Tue 3/9/21	635d		0d																									
CON.010	31	NTP to Contractor	Tue 10/2/18	Tue 10/2/18	0d	29FS+4d	0d																									
CON.020	32	Building Construction	Wed 10/3/18	Tue 1/26/21	605d	31	0d																									
CON.030	33	Substantial Completion	Tue 1/26/21	Tue 1/26/21	0d	32	0d																									
CON.040	34	Building Punch List	Wed 1/27/21	Tue 3/9/21	30d	33	0d																									
CON.050	35	Building Punch List Completion	Tue 3/9/21	Tue 3/9/21	0d	34	0d																									
OWO	36	<b>Owner Occupancy</b>	Wed 3/10/21	Wed 10/19/22	421d		0d																									
OWO.010	37	Furniture, Fit Out & Equipment	Wed 3/10/21	Tue 6/1/21	60d	35	0d																									
OWO.020	38	Owner Occupancy	Wed 6/2/21	Wed 6/2/21	0d	37FS+1d	0d																									
OWO.030	39	Warranty Period	Thu 6/3/21	Wed 10/19/22	360d	38	0d																									

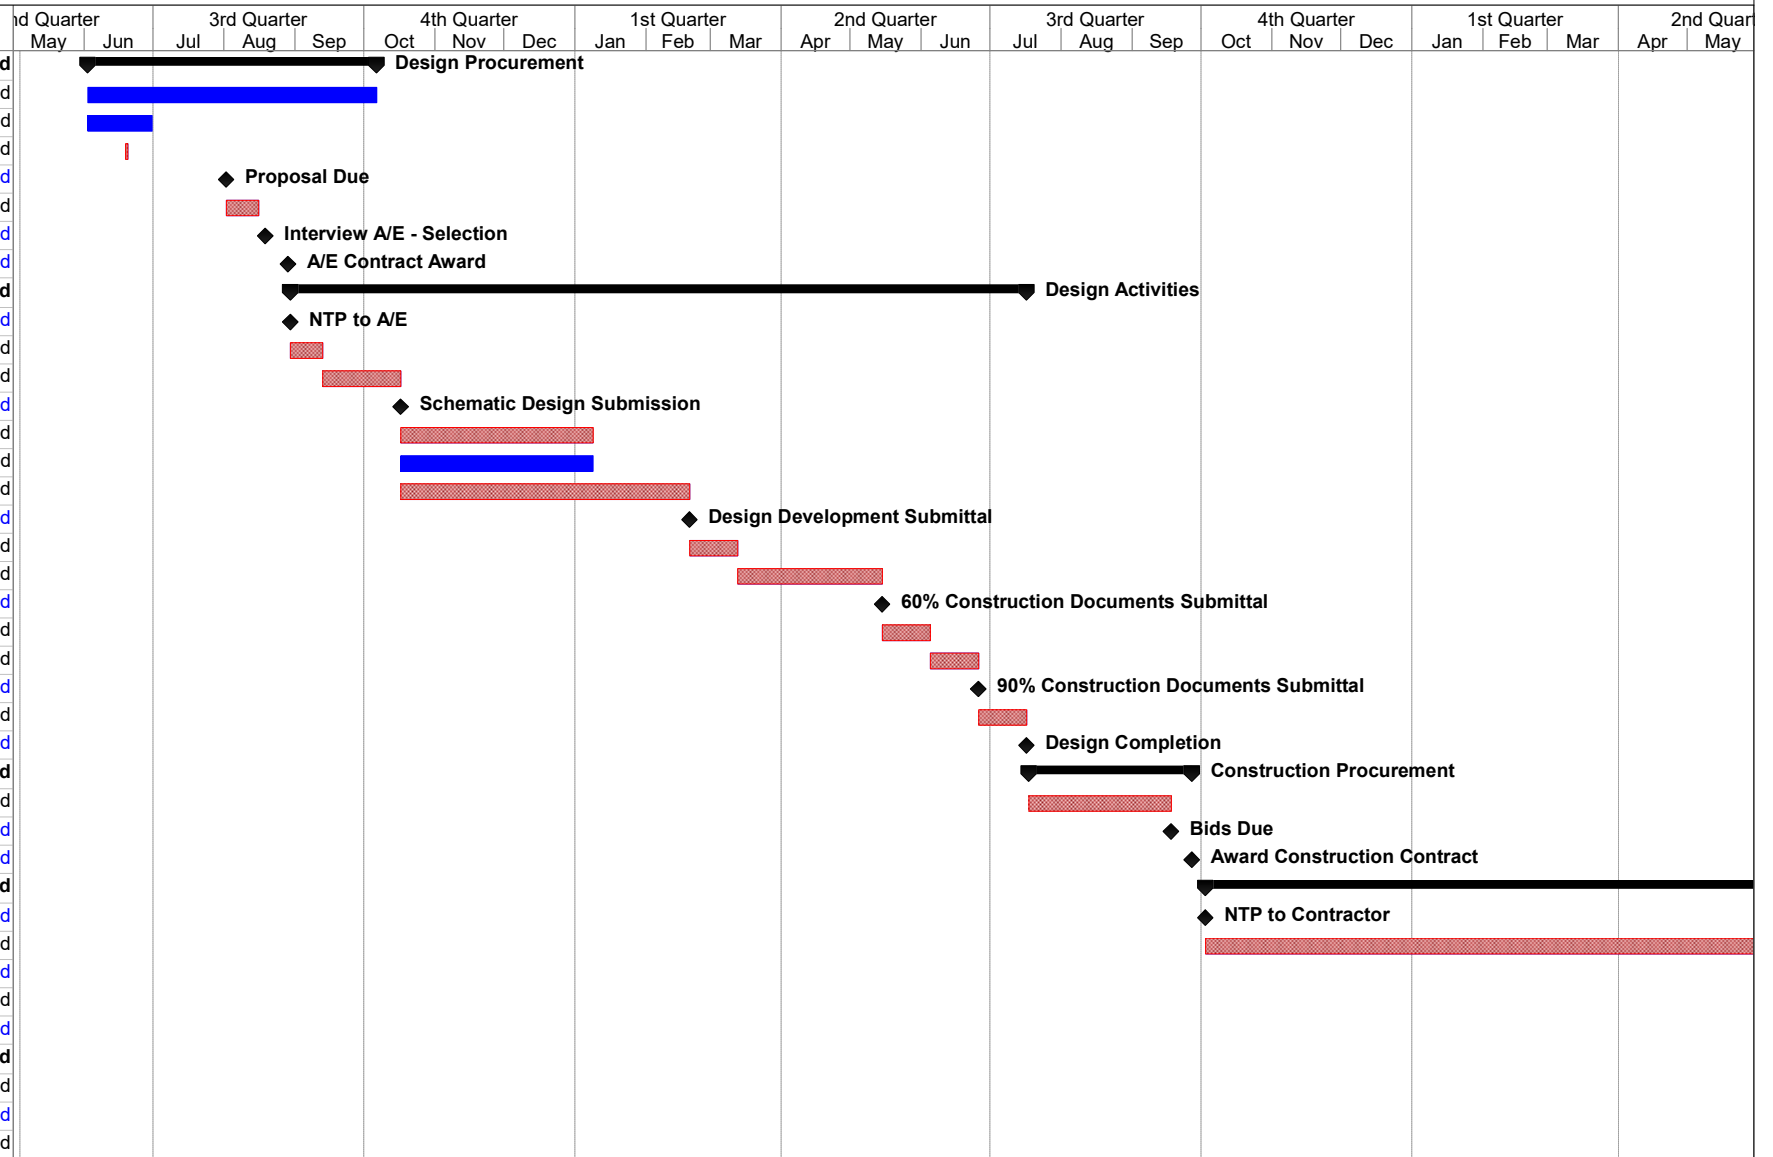

Task █ Milestone ◆ Summary ▬ Critical Path █

# CDR Maguire

## Franklin Regional Transit Authority -Critical Milestones

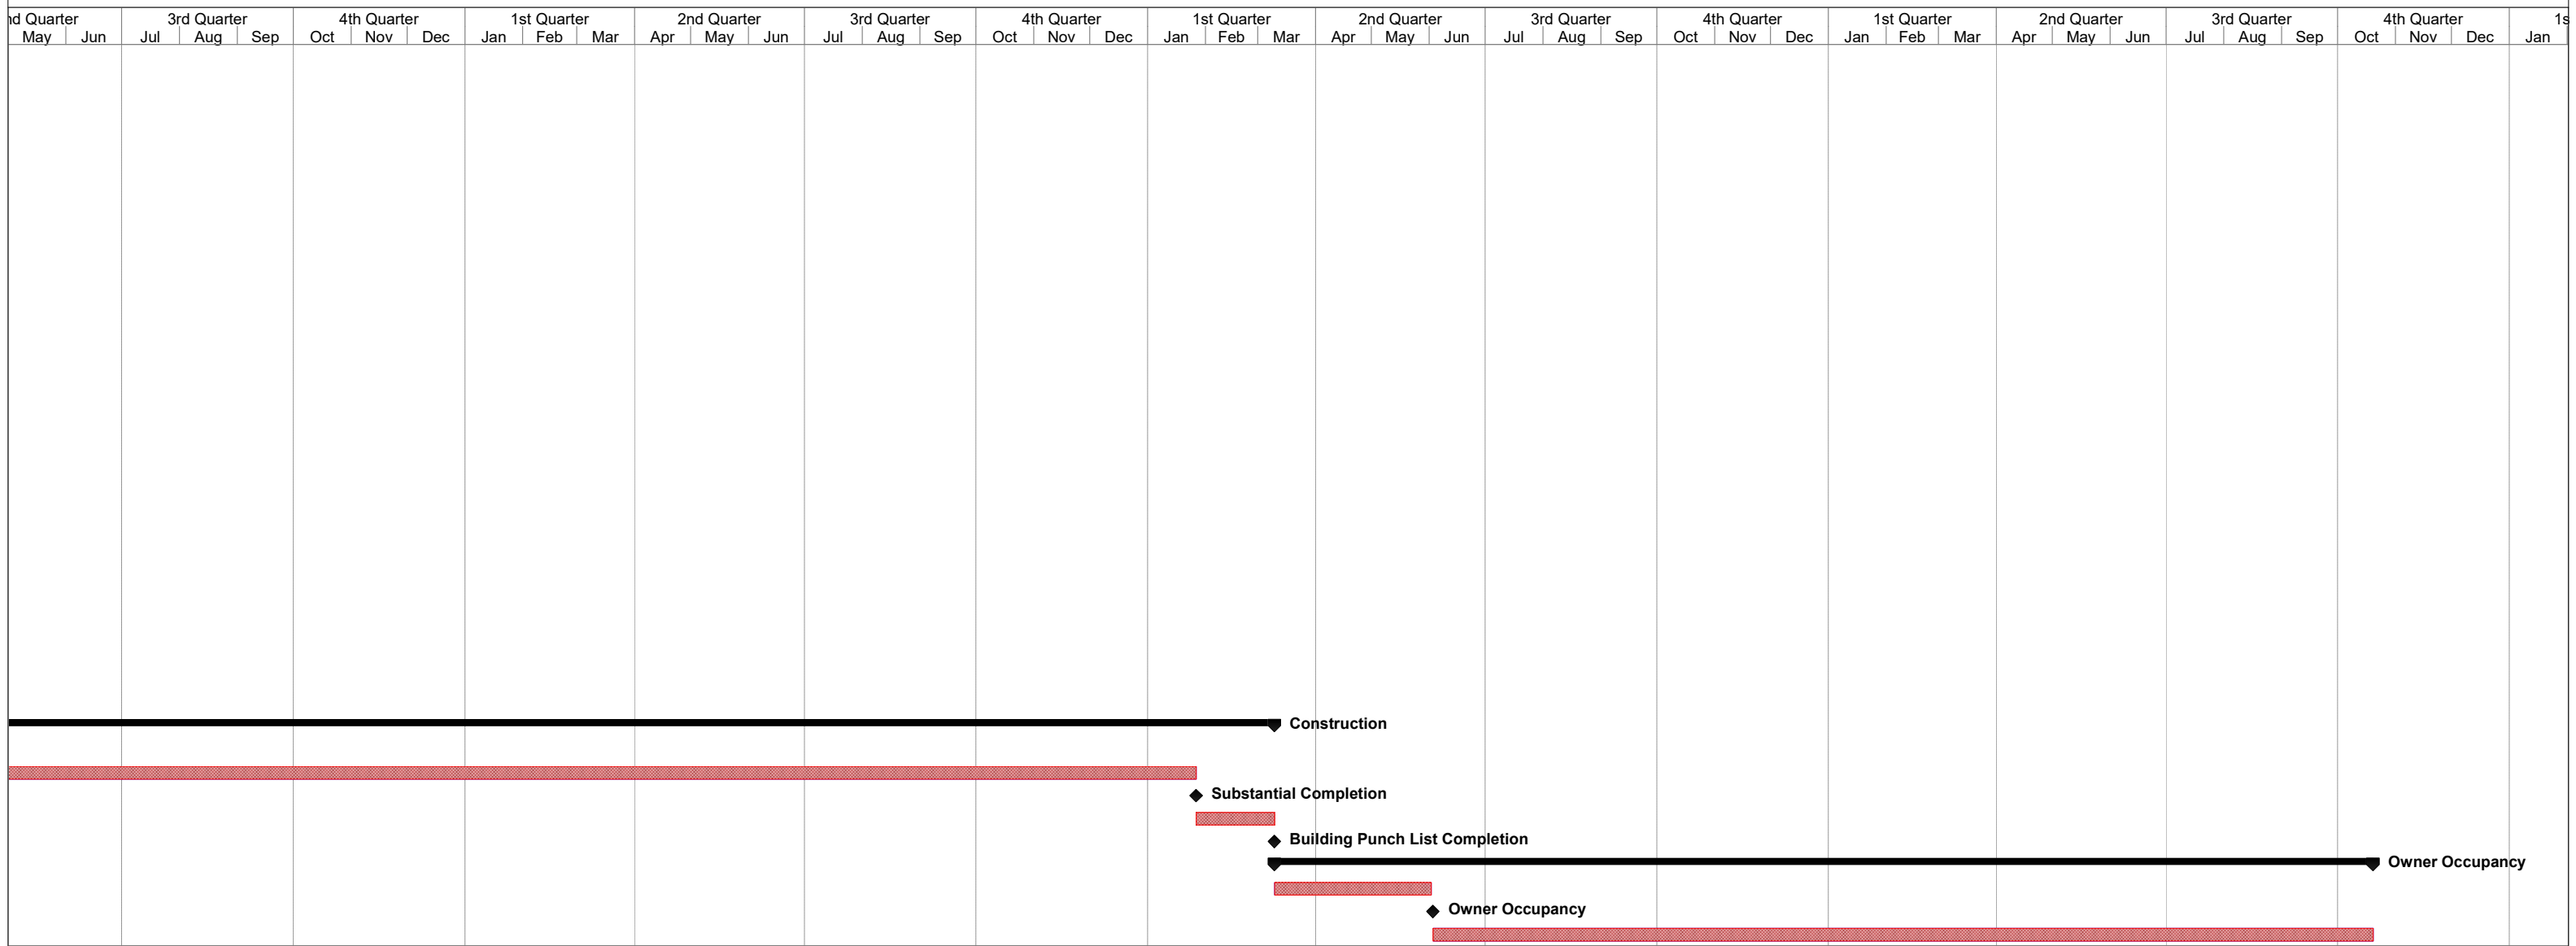

█ Task    
 ◆ Milestone    
  Summary    
 █ Critical Path
